CAMPUSRIDE

Sprint Execution Report

Sprint 1 and Sprint 2 | Planning, execution, progress and evidence

Project information	Details
Project	Campus Ride-Share Matching System (Campusride)
Team	Team 12
Team members	Pratham S Reddy • Piyush Shiv • Pravith Mohandas • Ramneek Gautam
Project repository	github.com/PiyushShiv26/SE-mini-project
Evidence set	18 chronological Jira board screenshots + 3 Jira project overview screenshots
Reporting snapshot	14 November 2026

Prepared from Jira progress screenshots and GitHub integration information supplied by the project team.

1. Executive summary

This report documents the planning and visible execution progress of Team 12 across two development sprints for Campusride. The first seven Jira screenshots (1–7) show Sprint 1 progression. Screenshots 8–18 show Sprint 2 progression. Three additional screenshots provide project-level context about overall work-item status, priorities, work types, workload distribution and epic progress.

Sprint 1	Sprint 2	Combined
8 of 8 issues shown Done	18 of 18 issues shown Done	26 sprint issues shown Done

The final Sprint 1 board snapshot shows all eight Sprint 1 issues in Done, with no issues remaining in To Do, In Progress or In Review. The final Sprint 2 board snapshot shows all 18 issues in Done, with no issues remaining in the other three columns. These are Jira status observations, not independent proof that every implementation, test or release activity passed.

1.1 Purpose and scope

The purpose of this report is to provide a consolidated record of sprint scope, observed status transitions, completed work categories and supporting Jira evidence. It supports the Software Engineering evaluation by making the team's iterative progress and delivery evidence easier to review. It does not replace the SRS, SAD, STP, test execution reports, pull-request review history or final product demonstration.

1.2 Evidence interpretation

Each screenshot is retained in the appendix in the same order supplied. Screenshots 1–7 are Sprint 1 evidence; screenshots 8–18 are Sprint 2 evidence. The three additional project overview screenshots follow the chronological board evidence. Where screenshots do not establish exact dates, duration, individual effort or test results, this report does not infer them.

2. Project and team context

Campusride is Team 12's campus ride-share matching system. The project brings together user management, ride management, booking management, communication and ratings, supported by testing and documentation work.

Team member	Project team
Pratham S Reddy	Team member
Piyush Shiv	Team member
Pravith Mohandas	Team member
Ramneek Gautam	Team member

The Jira project overview shows workload distribution across the named team members and an unassigned category. These percentages are a dashboard distribution snapshot, not a direct measurement of hours worked or an individual contribution score.

3. Sprint overview

Sprint	Evidence	Initial visible status	Final visible status	Main emphasis
Sprint 1	1–7	6 To Do; 1 In Review; 1 Done; 0 In Progress	8 Done; all other columns empty	Core account, ride and booking workflows; test-suite and setup review.
Sprint 2	8–18	11 To Do; 4 In Progress; 2 In Review; 0 Done	18 Done; all other columns empty	Integration, testing, cancellation, messaging, history, ratings, reports, docs, demo and UI polish.

4. Sprint 1 — Core workflows and initial verification

4.1 Progress observed in Jira

Screenshot 1 captures the early Sprint 1 board with six items in To Do, one item In Review and one item Done. Across screenshots 2–6, the board shows work moving into active development and review. Screenshot 7 provides the final Sprint 1 snapshot: eight items are in Done and the other workflow columns are empty. This progression is consistent with work being implemented, reviewed and then marked complete; the screenshots do not identify the duration spent in each status.

4.2 Sprint 1 work-item scope

Issue	Work item	Scope represented
CR-7	Verify registration and login workflows	User onboarding and authentication flow verification.

Issue	Work item	Scope represented
CR-8	Verify profile management	Profile-related user workflow verification.
CR-9	Complete ride creation and management	Driver-facing ride creation and management workflow.
CR-10	Complete ride search and filtering	Passenger-facing ride discovery and filtering workflow.
CR-12	Complete booking request workflow	Passenger booking request lifecycle.
CR-13	Complete driver booking decisions	Driver acceptance/rejection decision workflow.
CR-19	Audit existing automated test suite	Review of the automated testing baseline.
CR-29	Verify README and clean setup instructions	Repository setup and onboarding documentation.

4.3 Sprint 1 outcome

Sprint 1 concentrated on the foundational user journey: registering and signing in, maintaining a profile, creating and discovering rides, and requesting or deciding on bookings. The sprint also included a review of the existing automated tests and verification of repository setup instructions. All eight listed sprint issues appear in the final Done column. The sprint established the core ride-sharing workflows on which later integration and quality-assurance work could build.

5. Sprint 2 — Integration, testing and delivery

5.1 Progress observed in Jira

The earliest supplied Sprint 2 snapshot (image 8) shows 11 issues in To Do, four In Progress, two In Review and none Done. Subsequent screenshots show work progressing through implementation and review, with the Done column growing. Later snapshots include CR-31, the final evaluation readiness and development-freeze task, and CR-32, the UI redesign task. The final screenshot (image 18) shows 18 issues in Done and no issues in the other workflow columns.

5.2 Sprint 2 work-item scope

Issue	Work item	Scope represented
CR-11	Verify ride cancellation lifecycle	Ride lifecycle and cancellation behavior.
CR-14	Complete passenger booking cancellation	Passenger cancellation workflow.
CR-15	Verify seat availability and concurrency handling	Capacity consistency and concurrent booking behavior.
CR-16	Verify participant messaging	Communication between ride participants.
CR-17	Complete ride history and dashboard	Ride history and dashboard views.
CR-18	Verify ratings and reviews	Post-ride feedback functionality.
CR-20	Add and run backend integration tests	Backend integration testing.
CR-21	Run frontend unit tests	Frontend unit-test execution.
CR-22	Perform system validation testing	System-level validation.
CR-23	Generate code coverage report	Code coverage evidence.
CR-24	Generate branch coverage report	Branch coverage evidence.
CR-25	Prepare Unit Test Report	Documented unit-test results.
CR-26	Prepare System Validation Report	Documented system-validation results.
CR-27	Update Test Case Document	Update test cases to reflect implementation.
CR-28	Review SRS, SAD and STP against implementation	Requirements/design/test-plan consistency review.
CR-30	Prepare working-product demo video	Sprint 2 working-product demonstration.
CR-31	Conduct final evaluation readiness review and development freeze	Final readiness, documentation, evidence and freeze review.
CR-32	Redesign application UI and implement consistent dark theme	UI refinement and consistent dark visual theme.

5.3 Sprint 2 outcome

Sprint 2 expanded the project beyond the primary ride and booking flows. Its visible scope included cancellation behavior, seat-capacity and concurrency checks, participant messaging, ride history, ratings and reviews. It also emphasized integration and quality assurance through backend integration testing, frontend unit testing, system validation, code coverage and branch coverage.

Documentation and delivery activities formed another major part of the sprint: updating test cases, reviewing the SRS/SAD/STP against the implementation, preparing unit and system validation reports, and producing the Sprint 2 working-product video. The sprint scope also included the final readiness/development-freeze review and the dark-theme UI redesign. The final Jira board snapshot records 18 of 18 Sprint 2 issues as Done. Actual test outcomes and final pull-request integration must still be confirmed through execution logs and GitHub records.

6. Overall Jira project overview

The three additional screenshots provide a broader view of the Jira project beyond the two sprint boards. They show a project summary dashboard, a status/recent-activity dashboard, and a list view of higher-level work items.

6.1 Work-item status and activity

One overview screenshot displays 32 total work items, with the status chart showing all 32 as Done. The recent-activity panel shows status updates to project epics, including User Management, Ride Management and Booking Management. This project-level dashboard snapshot is separate from the sprint-specific counts of eight and 18.

6.2 Work type and priority distribution

The project summary dashboard displays a work-type distribution of approximately 47% Tasks, 34% Stories and 19% Epics. The priority chart shows work concentrated in the High category, with additional Highest and Medium priority items. These are dashboard summaries at the time of capture.

6.3 Team workload and epic progress

The workload panel shows Pratham S Reddy (25%), Pravith Mohandas (22%), Piyush Shiv (19%), Ramneek Gautam (16%) and Unassigned (19%). Percentages may not sum to exactly 100 due to rounding. The dashboard also displays 100% progress for the visible epics CR-5 Testing and Quality Assurance, CR-6 Documentation and Delivery, and CR-3 Booking Management.

The list view shows six top-level epics, all marked Done: CR-6 Documentation and Delivery, CR-3 Booking Management, CR-5 Testing and Quality Assurance, CR-1 User Management, CR-4 Communication and Ratings, and CR-2 Ride Management.

7. GitHub delivery and integration evidence

Jira provides sprint planning and status evidence, while GitHub provides repository history and integration evidence. The team separately confirmed the following delivery facts:

Deliverable	GitHub evidence supplied	Interpretation
Sprint 2 demo video	Committed at src/docs/videos/Campusride_Demo_Sprint2.mp4; PR #33 merged.	The demo video is integrated into main according to the supplied Git history.
Dark-theme UI redesign	Commit b1214a9 is reachable from main; PR #32 was shown as merged.	The UI changes are present in main even though the commit history does not show a separate merge commit for PR #32.
Final readiness work	Branch chore/CR-31-final-evaluation-readiness; PR #34 was reported open and awaiting review/merge.	Jira may show CR-31 as Done, but final GitHub integration remains dependent on PR review and merge.

Marking an issue Done in Jira does not automatically mean its pull request has been merged or all final validation has passed. CR-31 should be treated as pending final integration until PR #34 is reviewed, merged and verified on main.

8. Sprint-level observations

• Incremental completion: the screenshots show work items moving from To Do through In Progress and In Review to Done rather than all work being marked complete at once.

• Core-to-quality progression: Sprint 1 focused on foundational ride-sharing journeys; Sprint 2 broadened the scope to integration, lifecycle edge cases, testing, documentation and release readiness.

• Cross-functional delivery: the sprint scope spans frontend experience, backend behavior, data consistency, automated testing, documentation and demonstration deliverables.

• Traceable project status: Jira provides a visible status trail, while GitHub commits and pull requests provide repository-level integration evidence.

9. Conclusion

Based on the supplied Jira evidence, Team 12 completed the visible Sprint 1 scope of eight issues and the visible Sprint 2 scope of 18 issues. Sprint 1 established the principal user, ride and booking workflows. Sprint 2 extended those workflows, addressed integration and quality assurance, updated project documentation, produced the Sprint 2 demo video and refined the application UI. The additional Jira overview screenshots show 32 project work items marked Done, six top-level epics marked Done, and dashboard summaries for work type, priority, workload and epic progress.

Before final submission, the team should ensure that CR-31 has been reviewed and merged, that the final main branch passes the required checks, and that testing and coverage reports accurately reflect the final integrated code. This report records Jira progress evidence and does not substitute for final verification artifacts.


10. Evidence limitations

The report is based on screenshots and GitHub facts supplied by the project team. The screenshots do not independently establish exact sprint start/end dates, time spent per issue, all assignee changes, actual test execution results, code coverage values, or completeness of every pull-request review. Those details should be substantiated with Jira issue history, GitHub PR timelines, CI logs and final testing reports if requested during evaluation.


Appendix A — Chronological Jira screenshot evidence

The 18 sprint-progress screenshots are reproduced in their original numbered order: screenshots 1–7 correspond to Sprint 1 and screenshots 8–18 correspond to Sprint 2. The three project overview screenshots follow. Two screenshots are placed on each appendix page and enlarged to use the available page area.


Screenshot 01 — Sprint 1

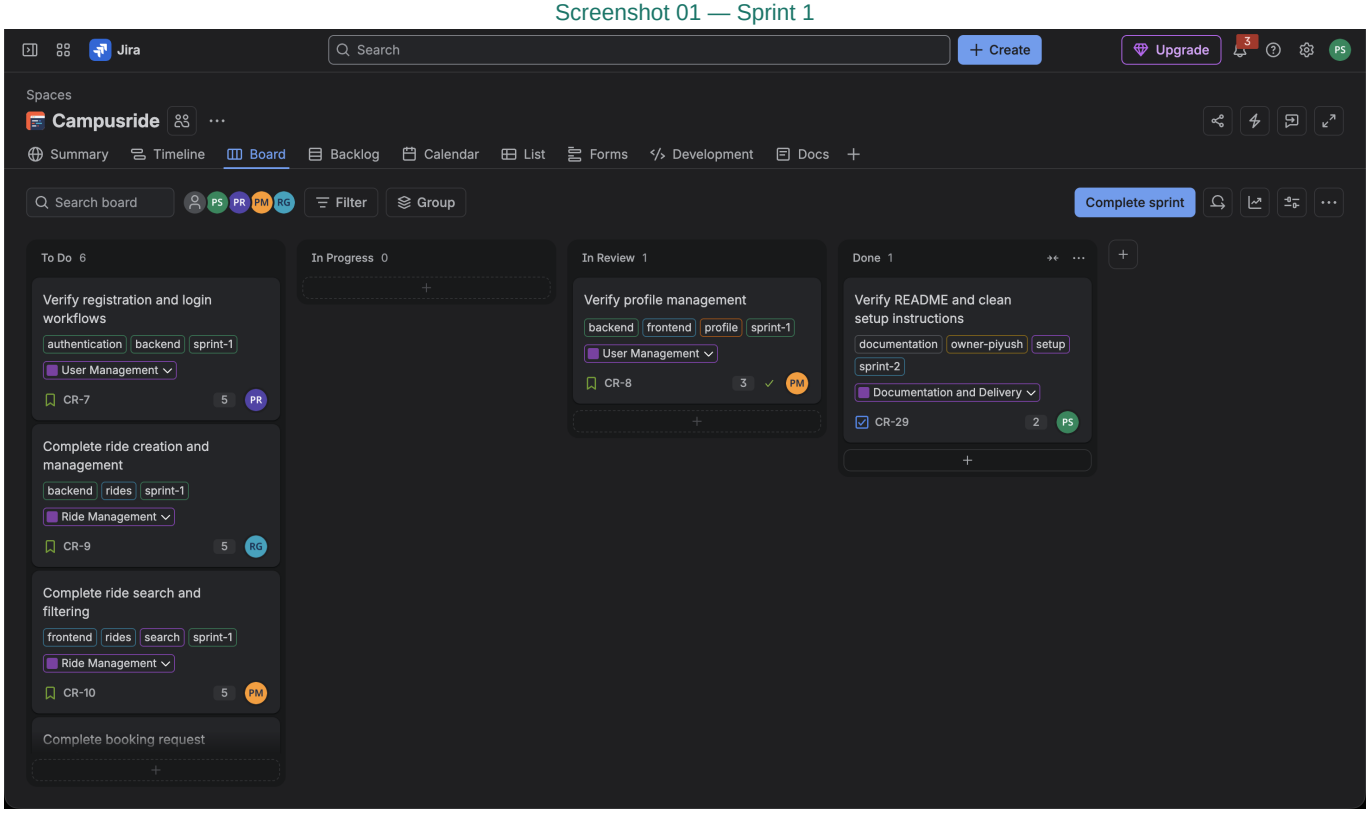


Screenshot 02 — Sprint 1

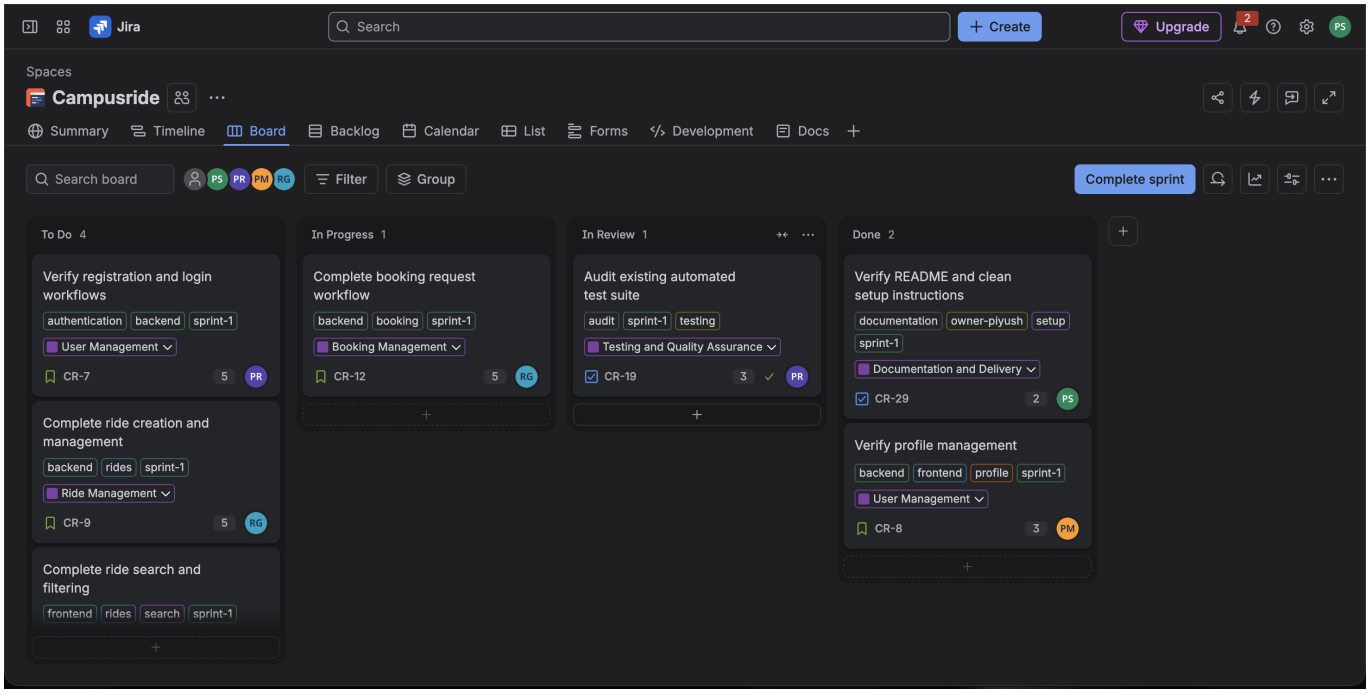


Screenshot 03 — Sprint 1

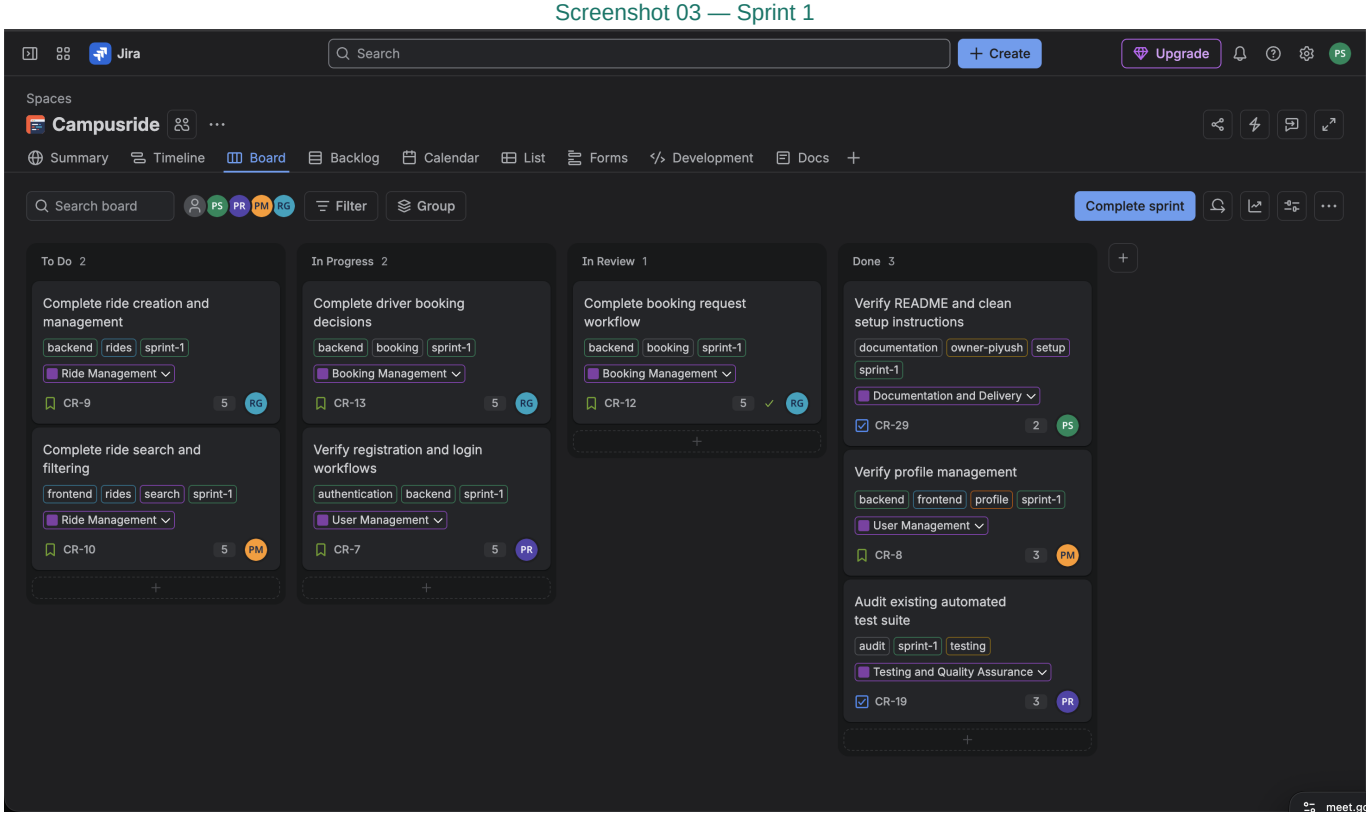


Screenshot 04 — Sprint 1

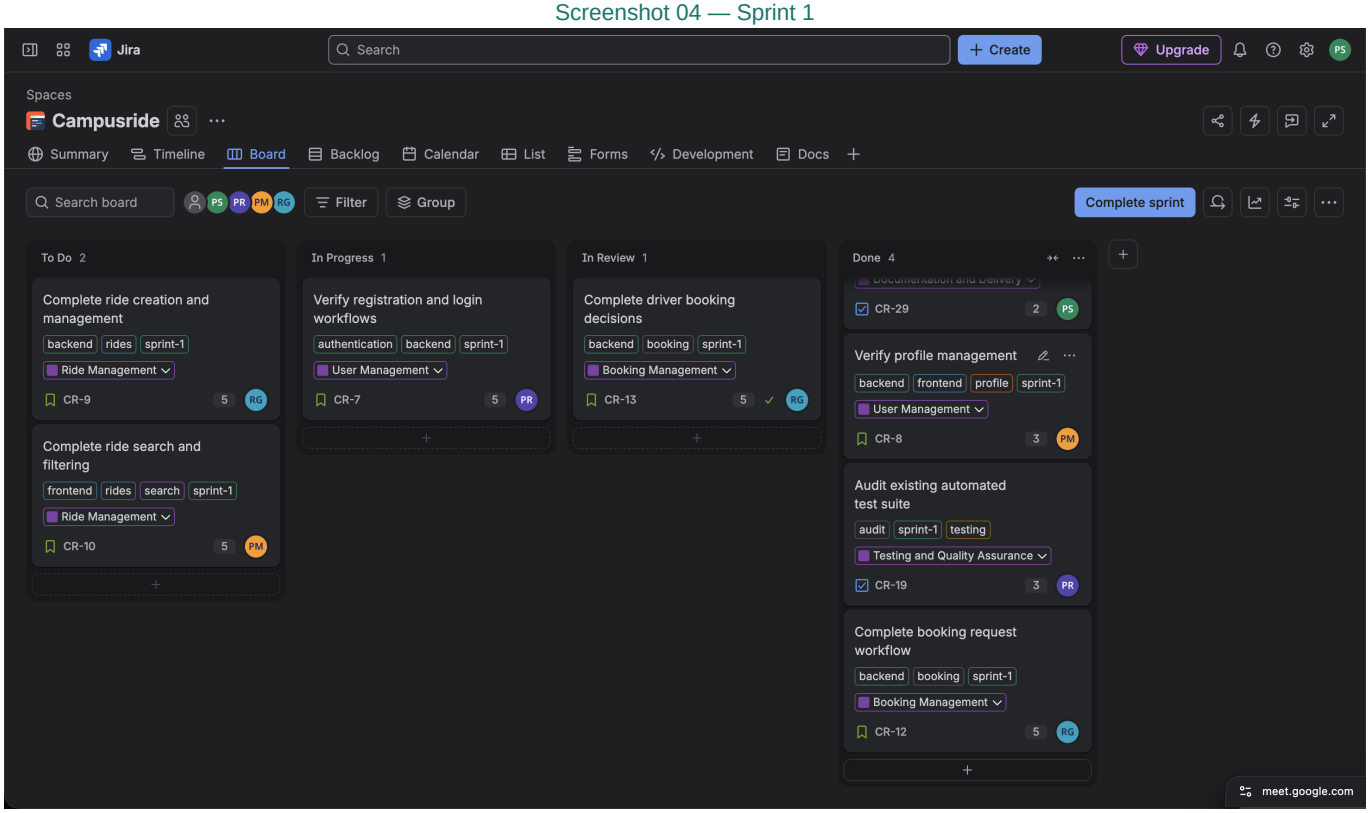


Screenshot 05 — Sprint 1

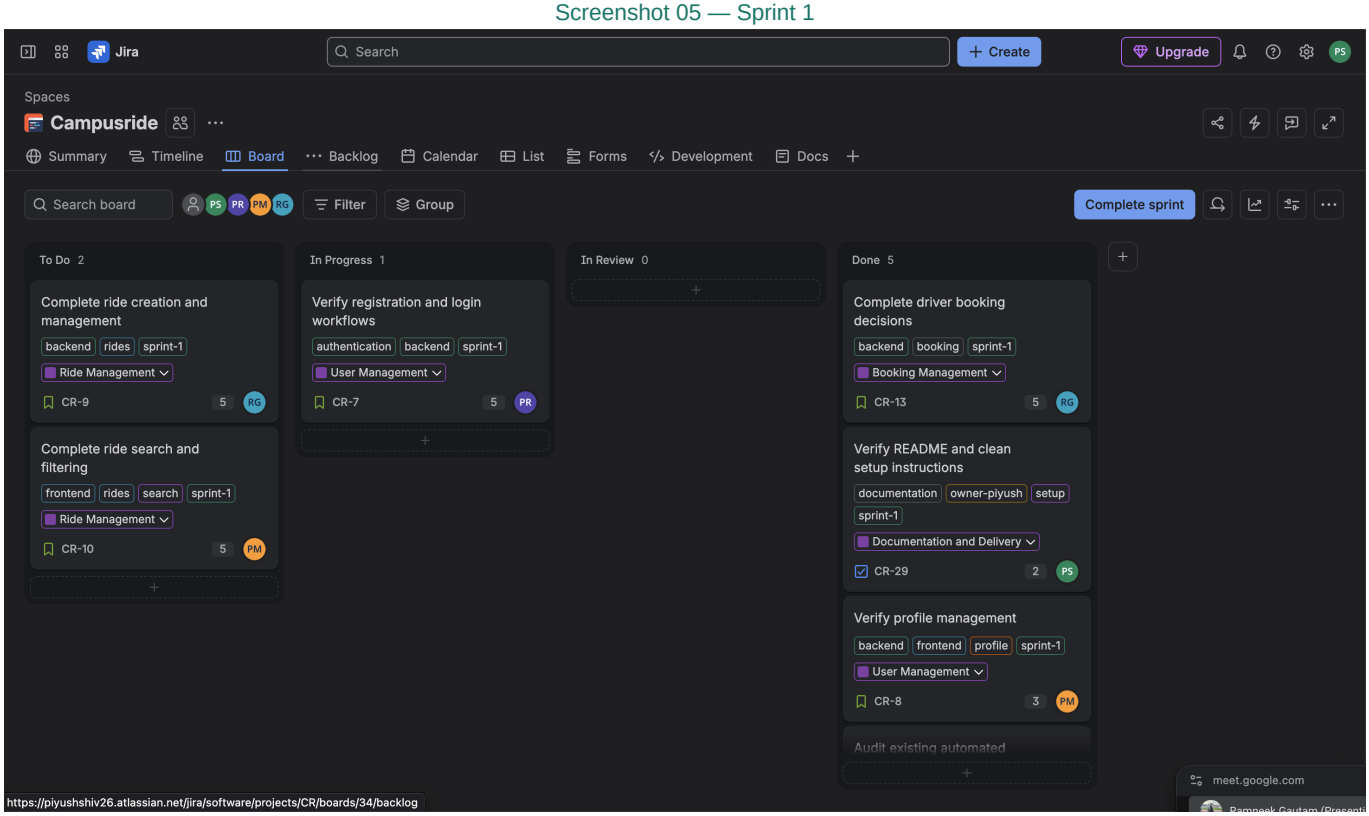


Screenshot 06 — Sprint 1

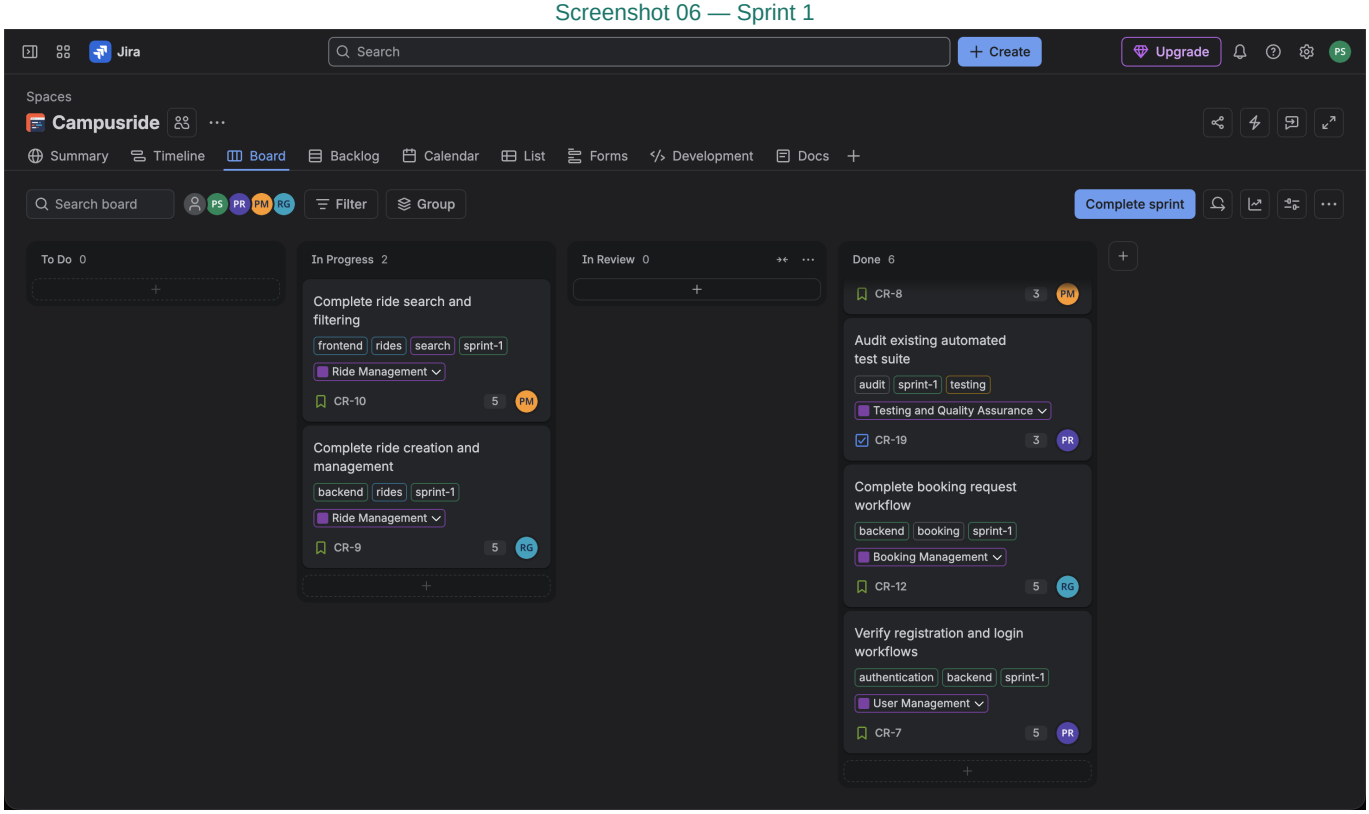


Screenshot 07 — Sprint 1

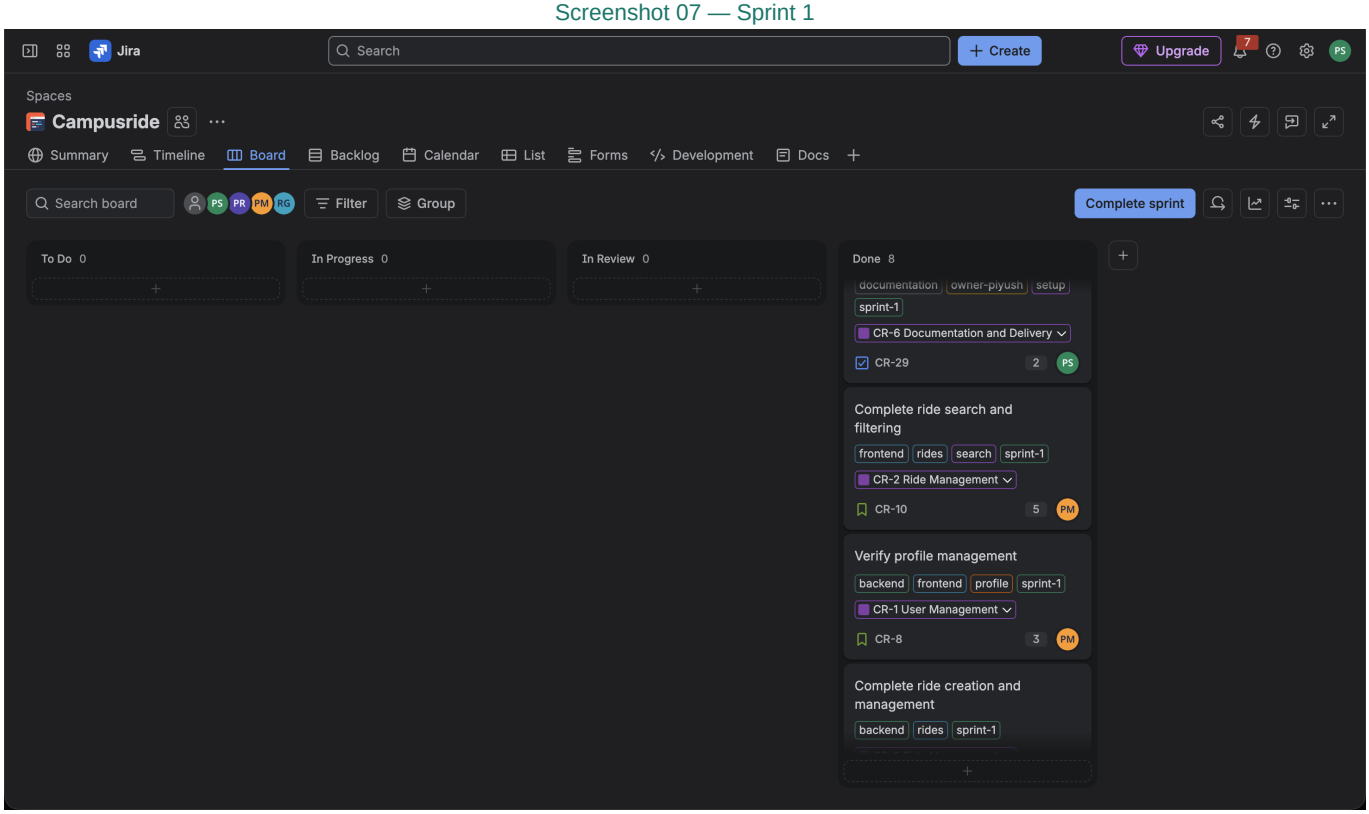


Screenshot 08 — Sprint 2

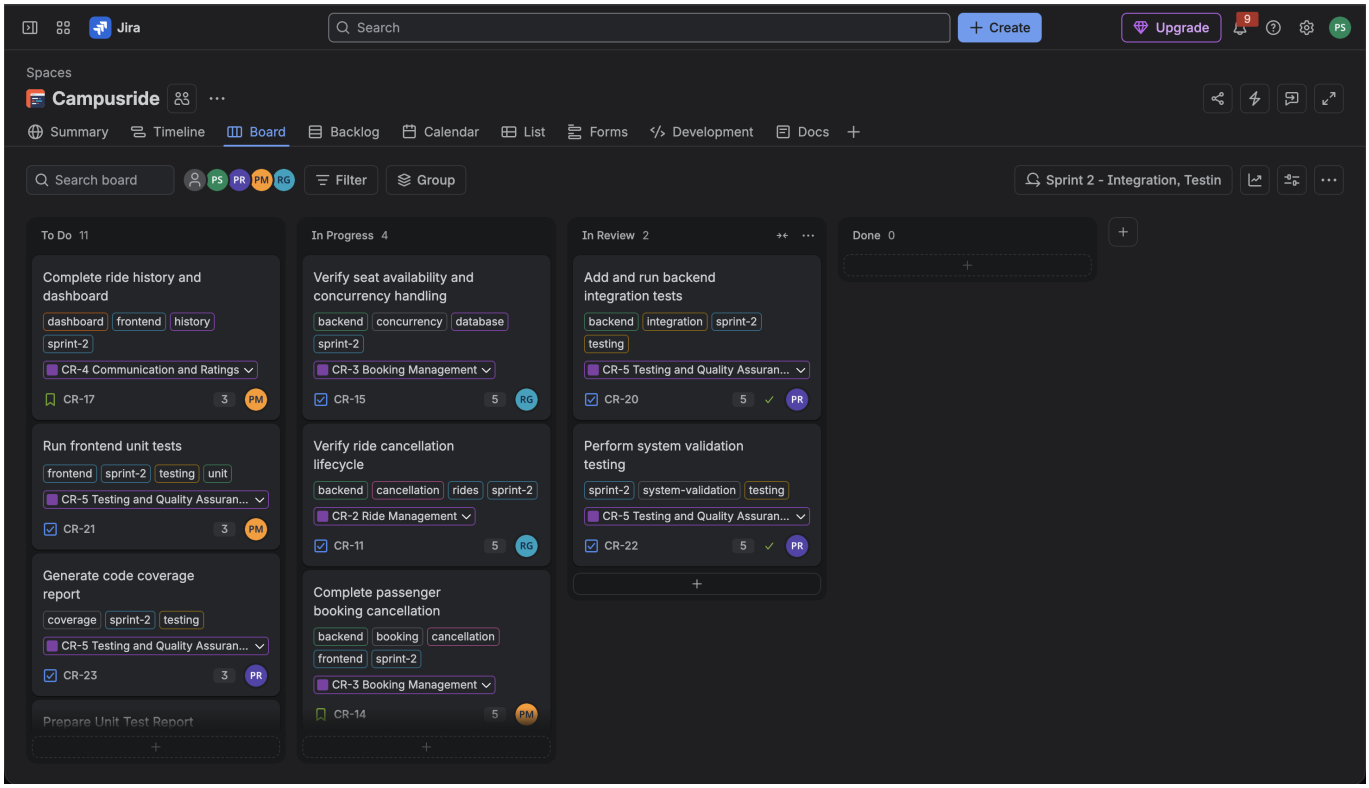


Screenshot 09 — Sprint 2

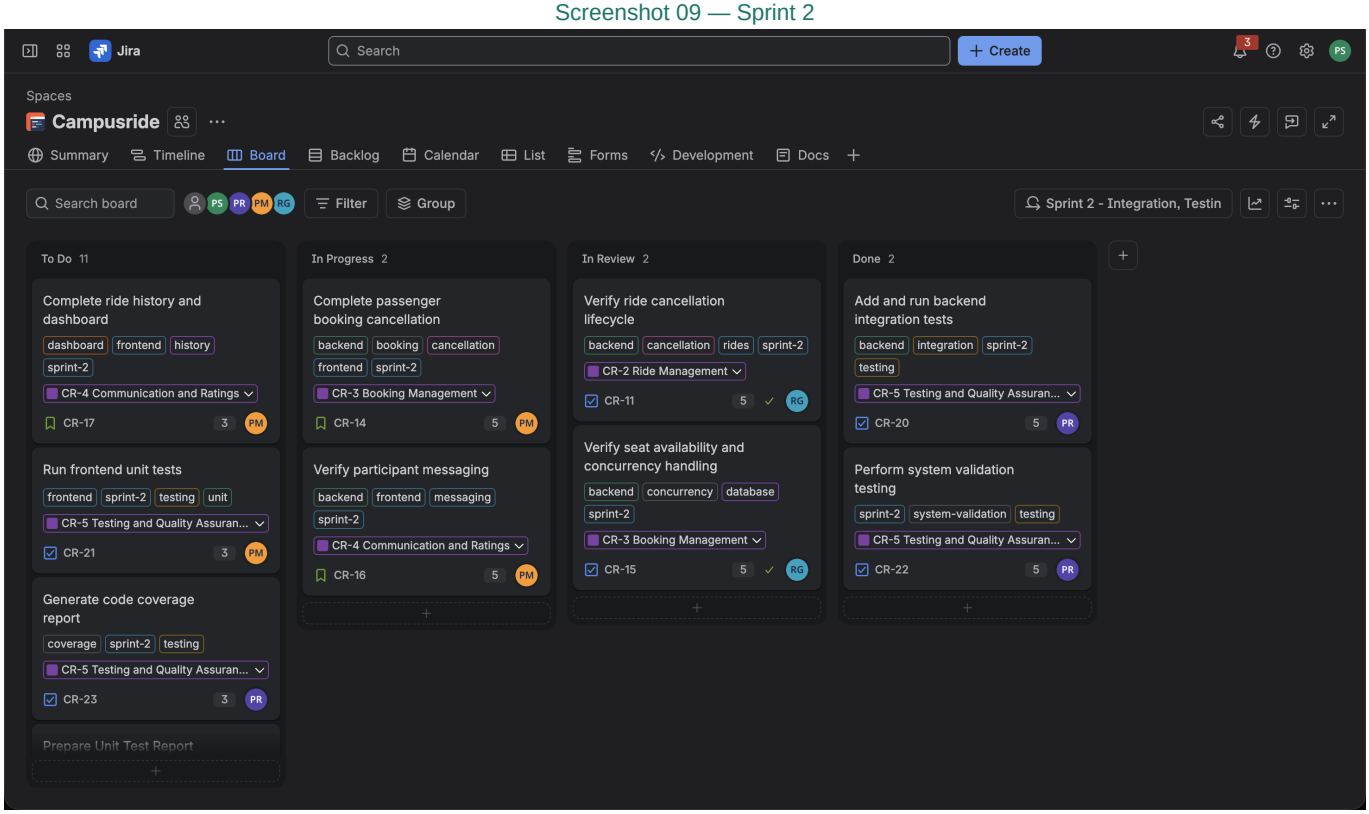


Screenshot 10 — Sprint 2

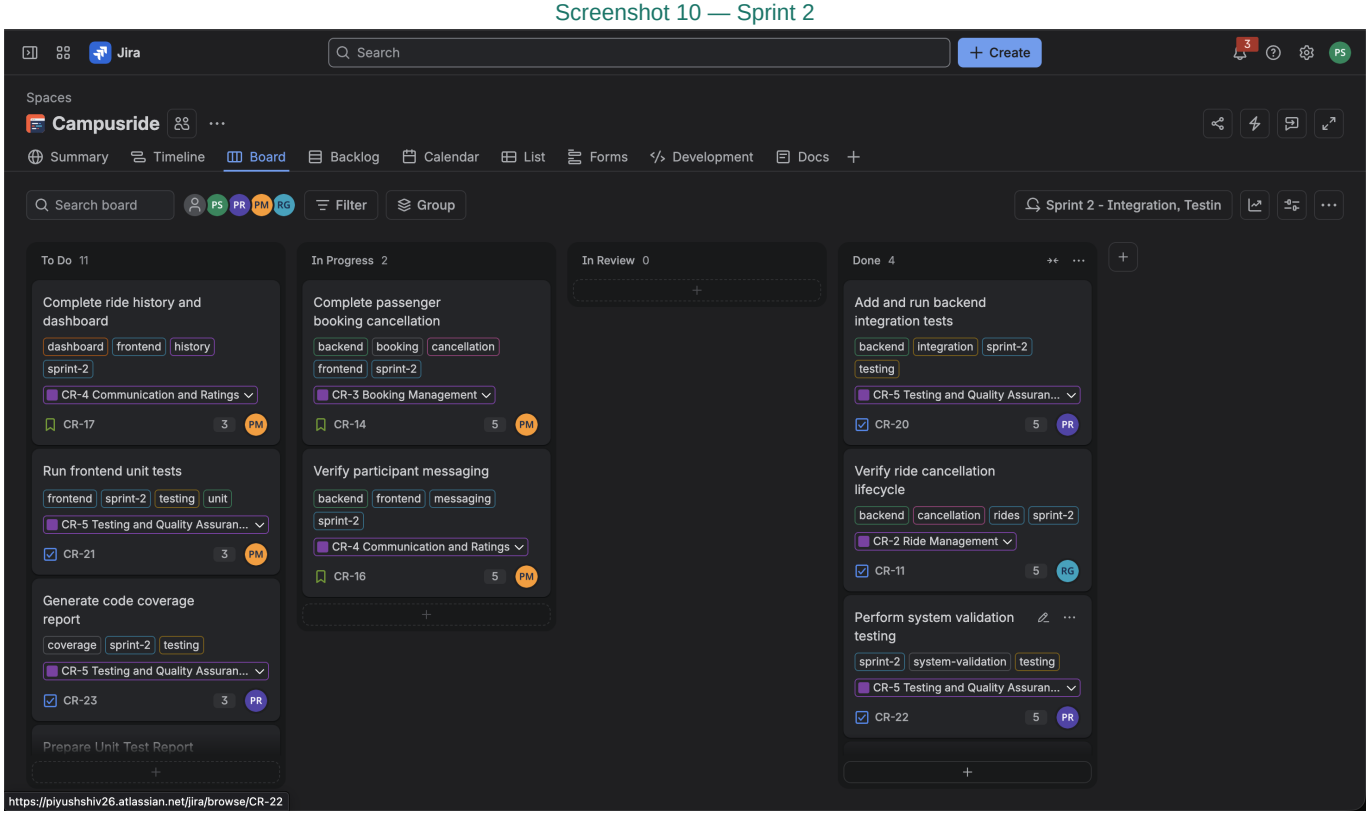


Screenshot 11 — Sprint 2

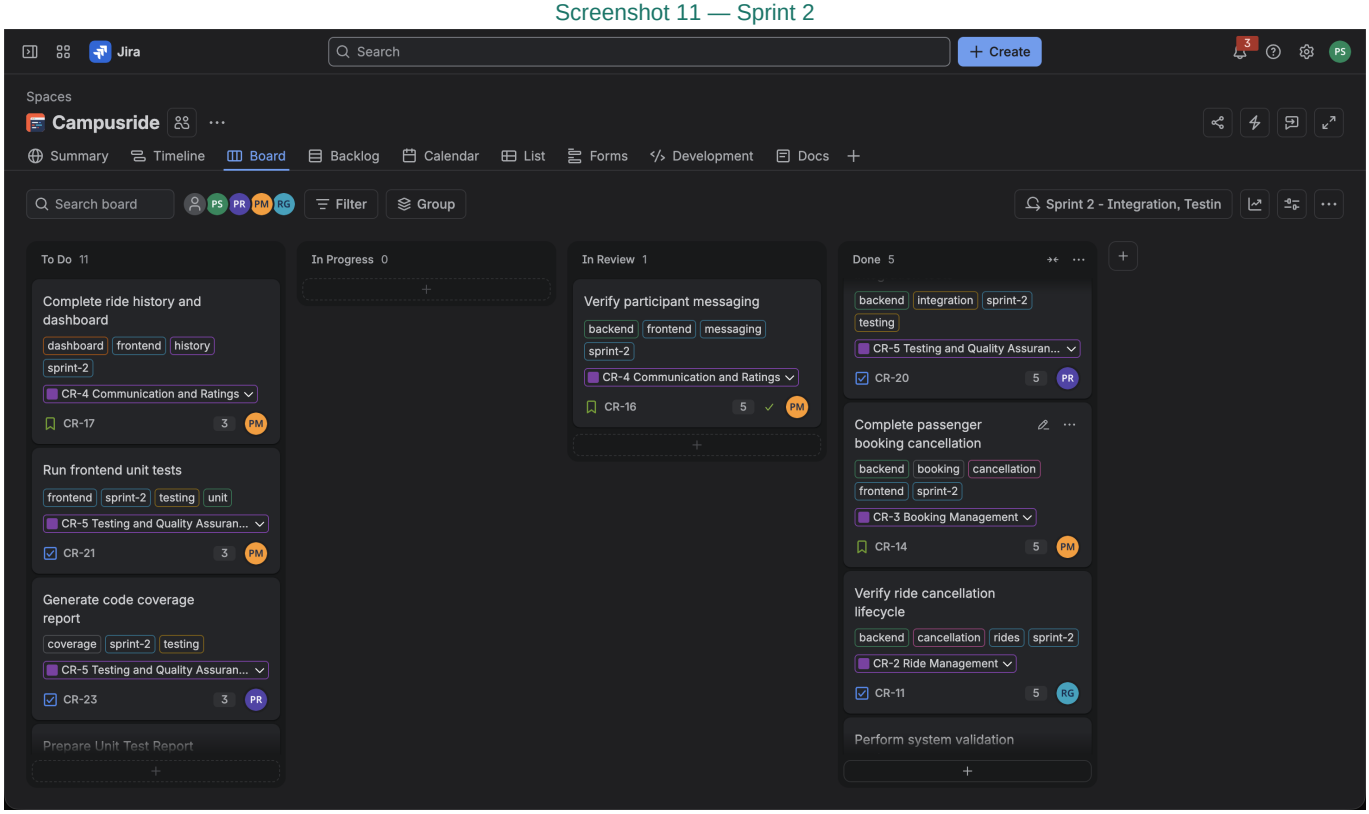


Screenshot 12 — Sprint 2

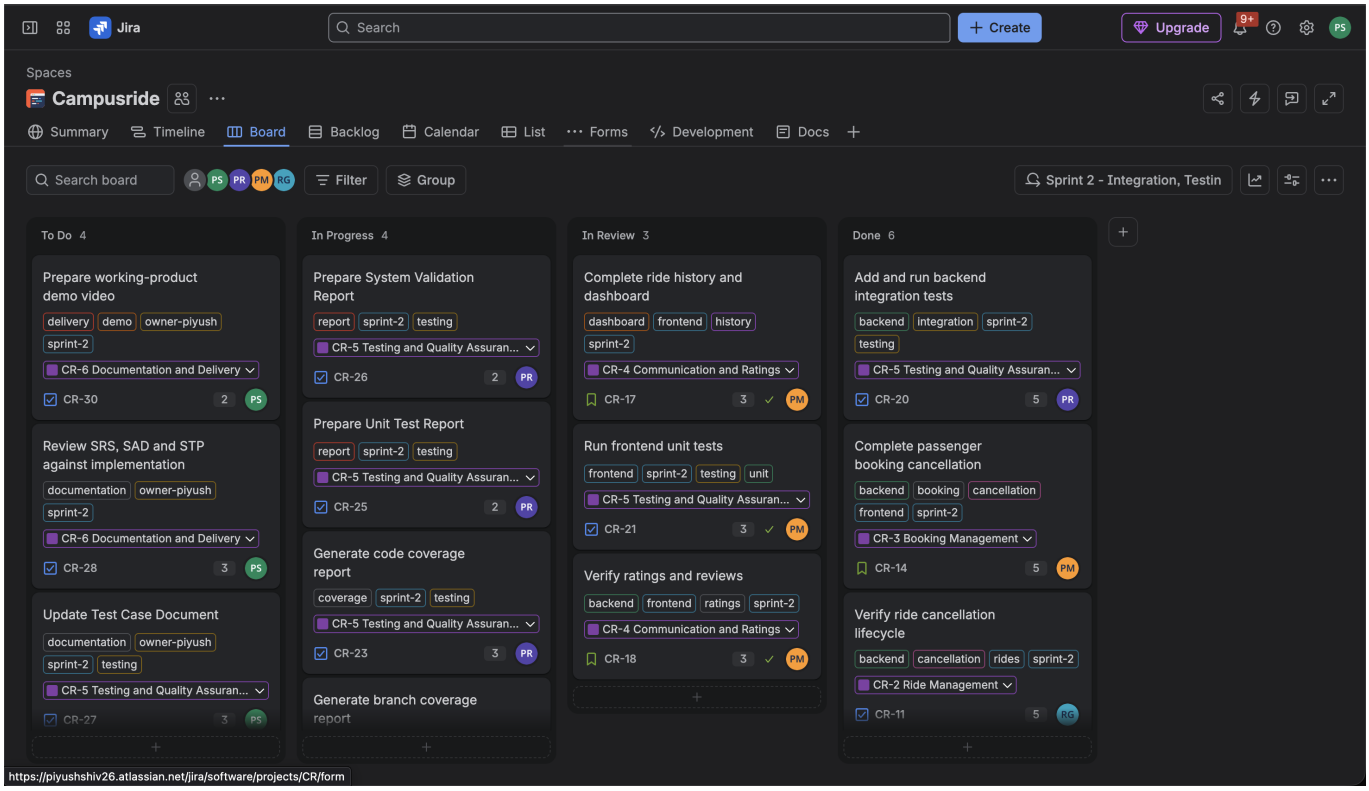


Screenshot 13 — Sprint 2

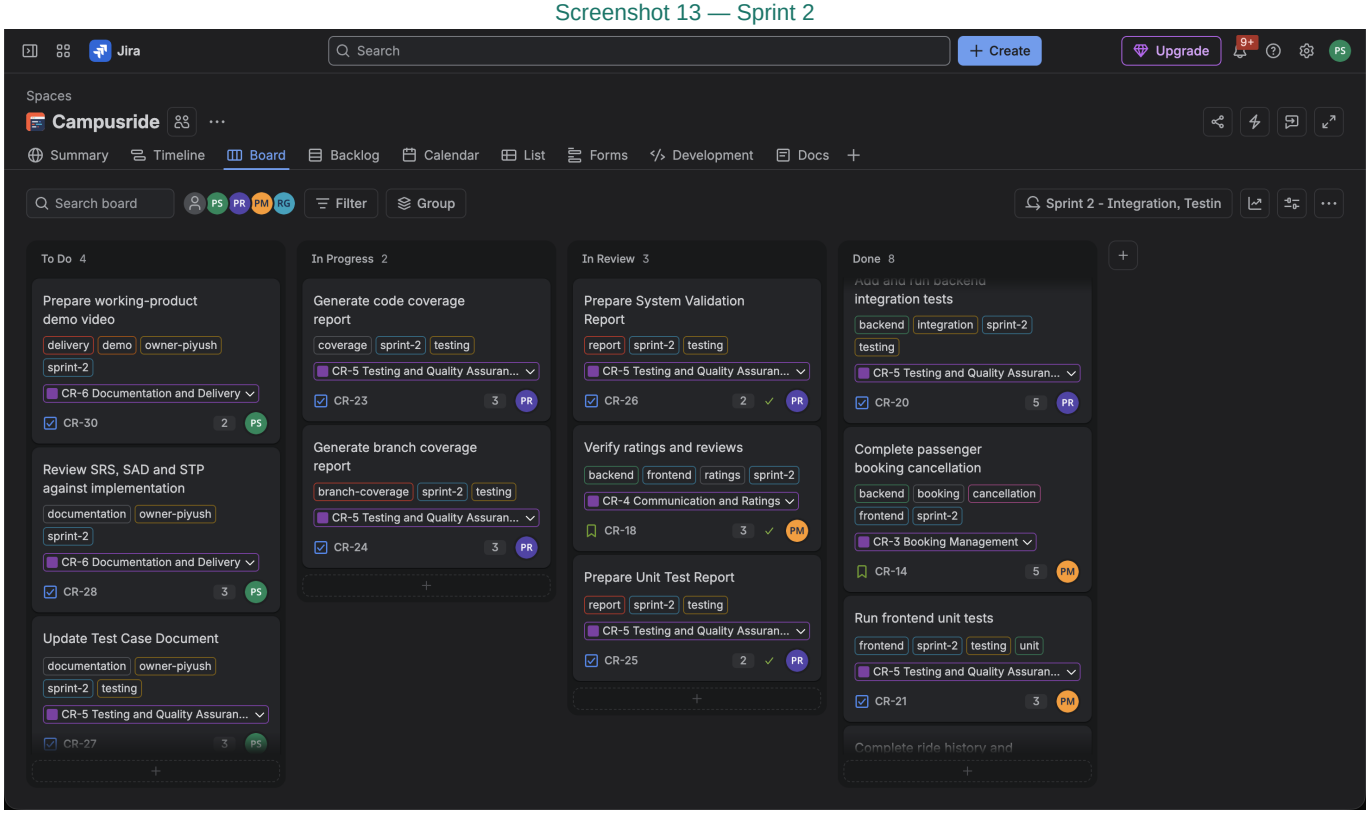


Screenshot 14 — Sprint 2

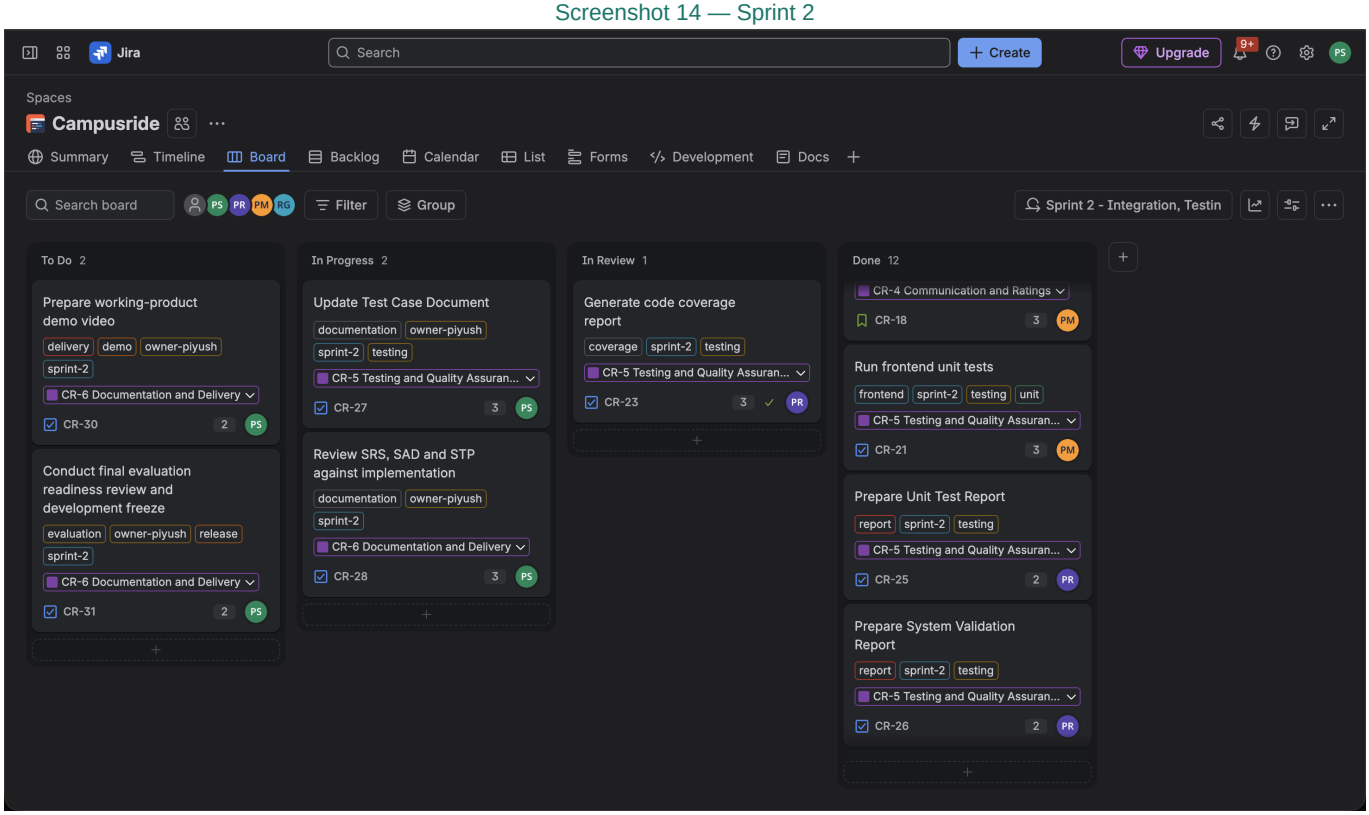


Screenshot 15 — Sprint 2

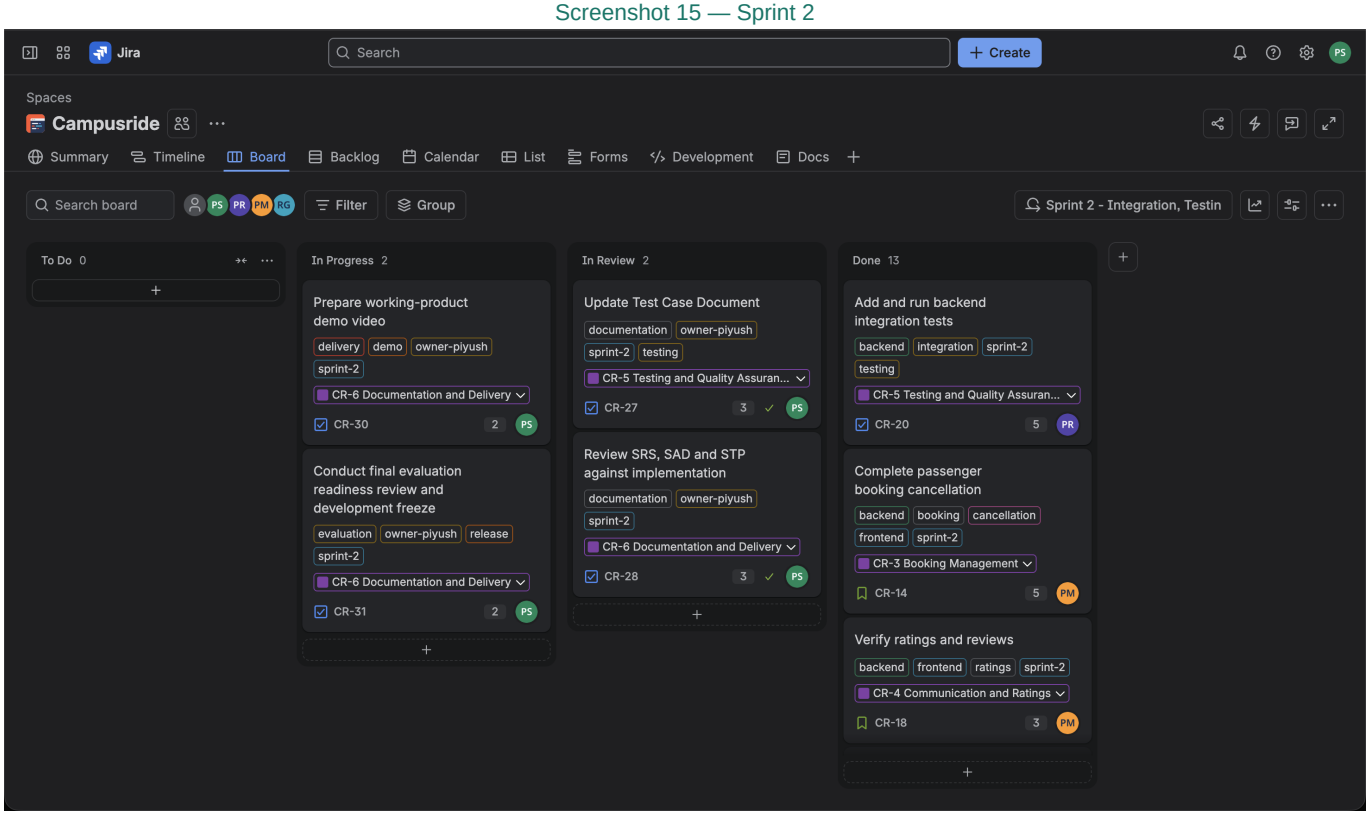


Screenshot 16 — Sprint 2

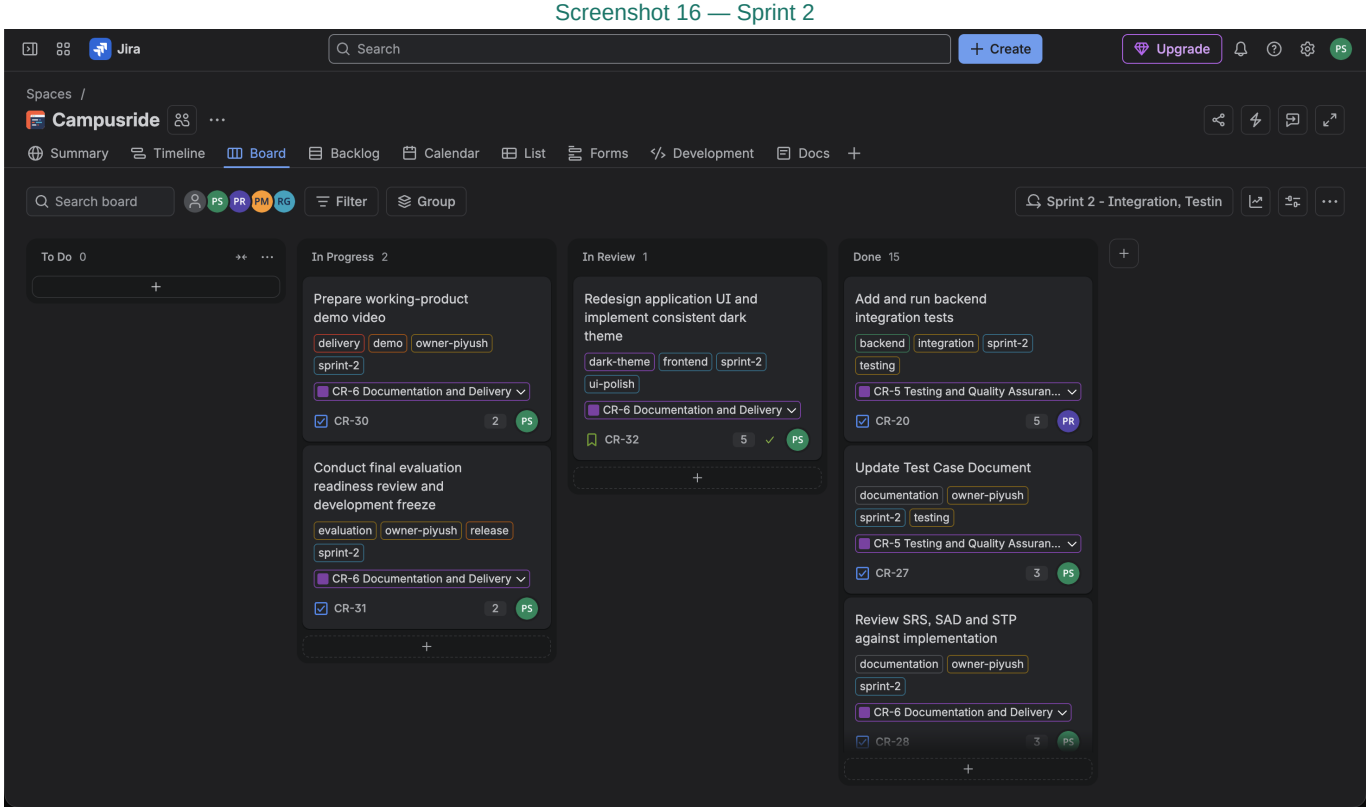


Screenshot 17 — Sprint 2

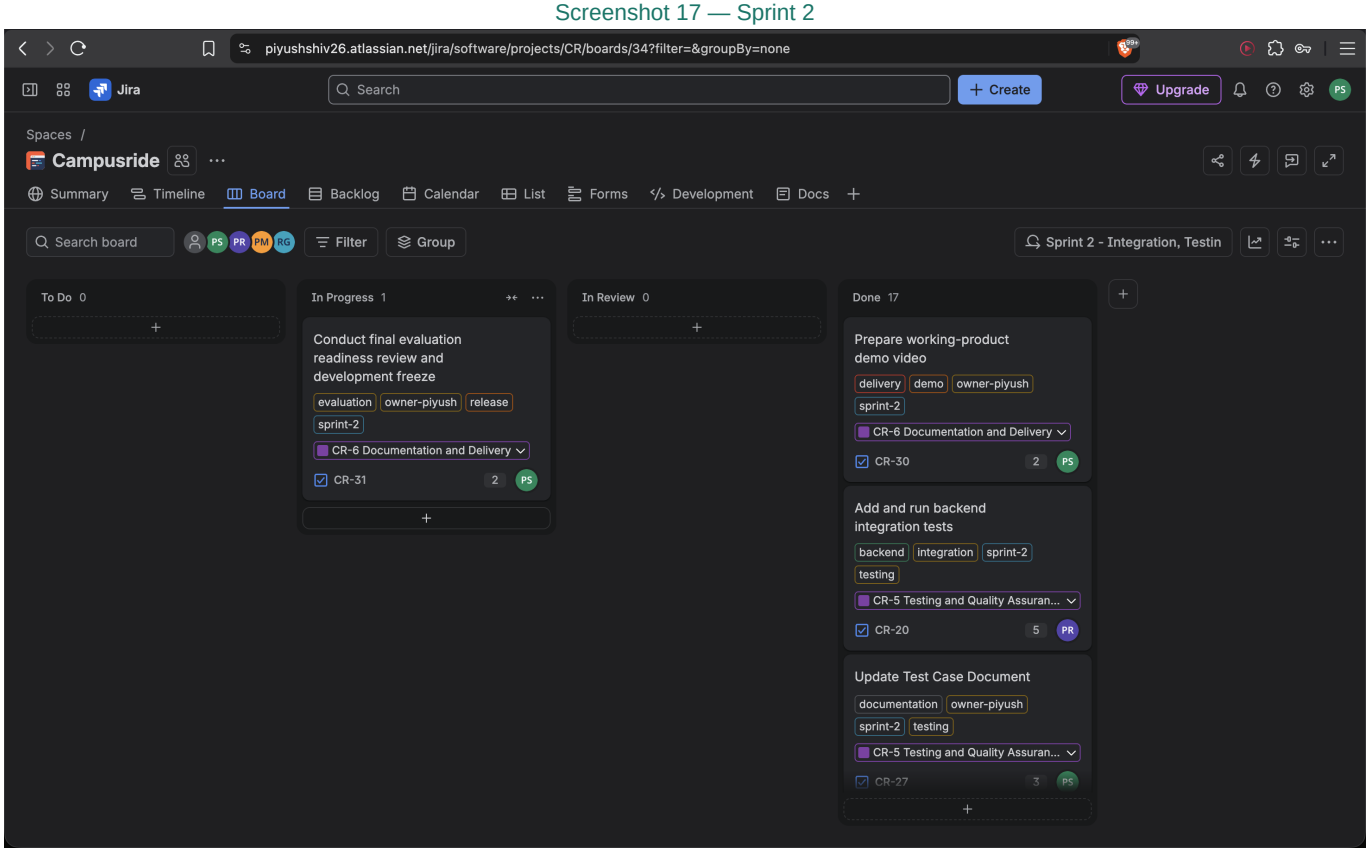


Screenshot 18 — Sprint 2

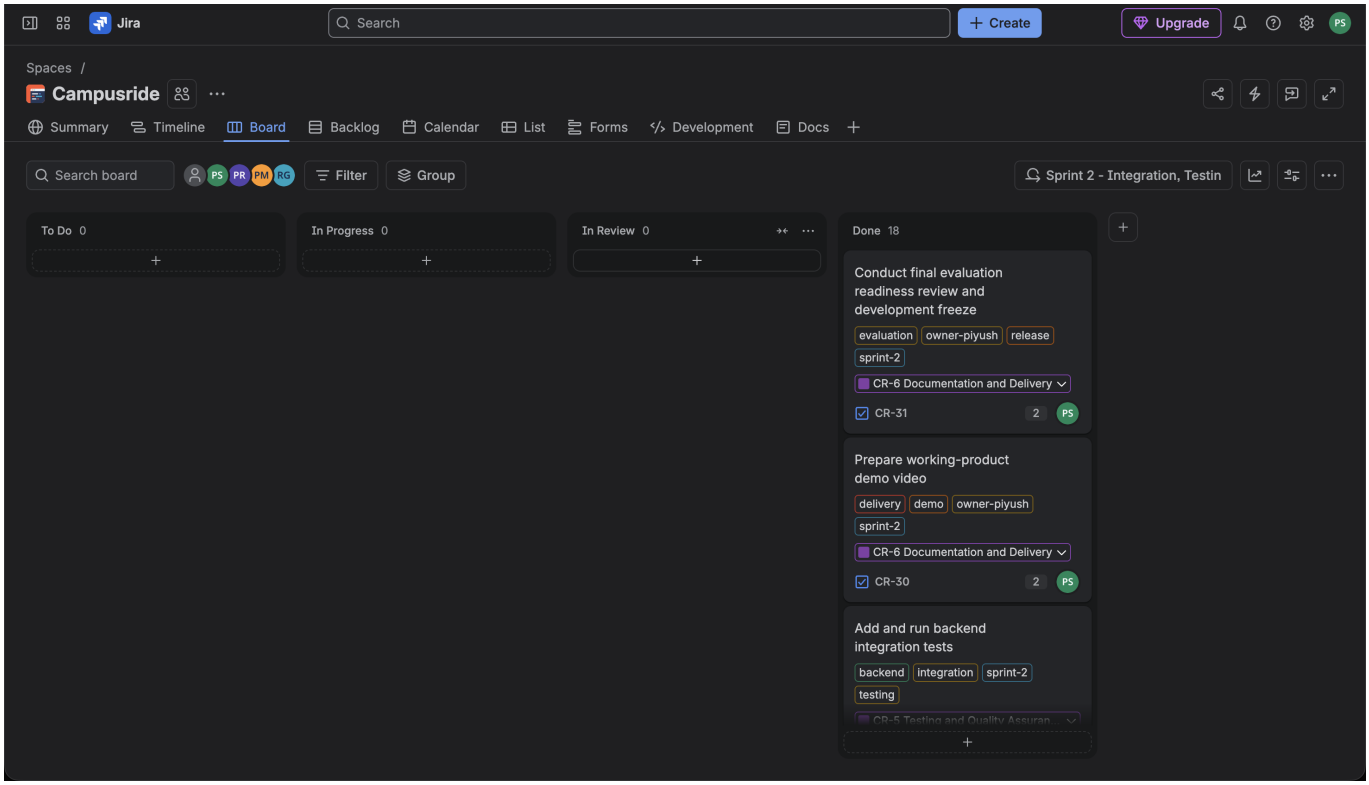

Additional Jira overview — priority, work types, workload and epic progress

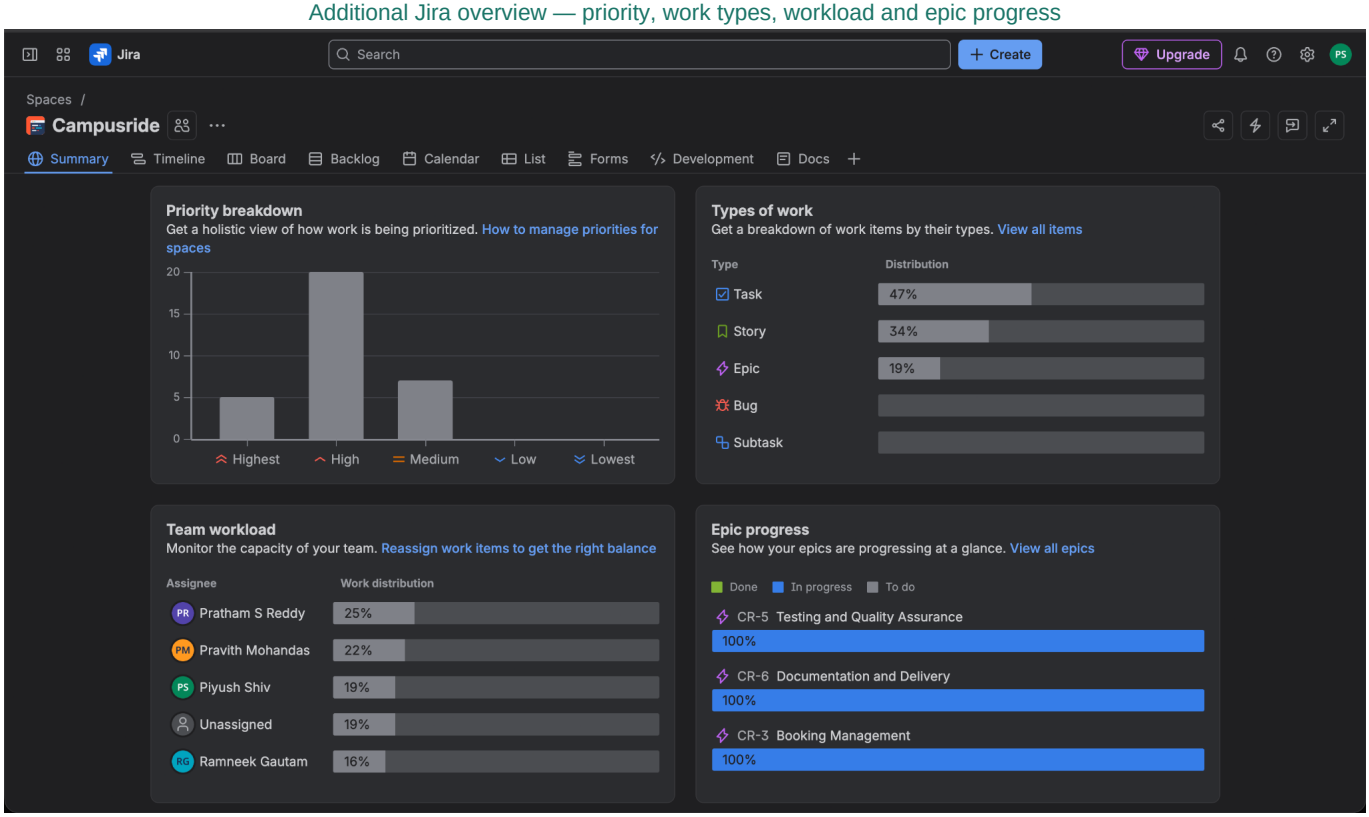

Additional Jira overview — overall work-item status and recent activity

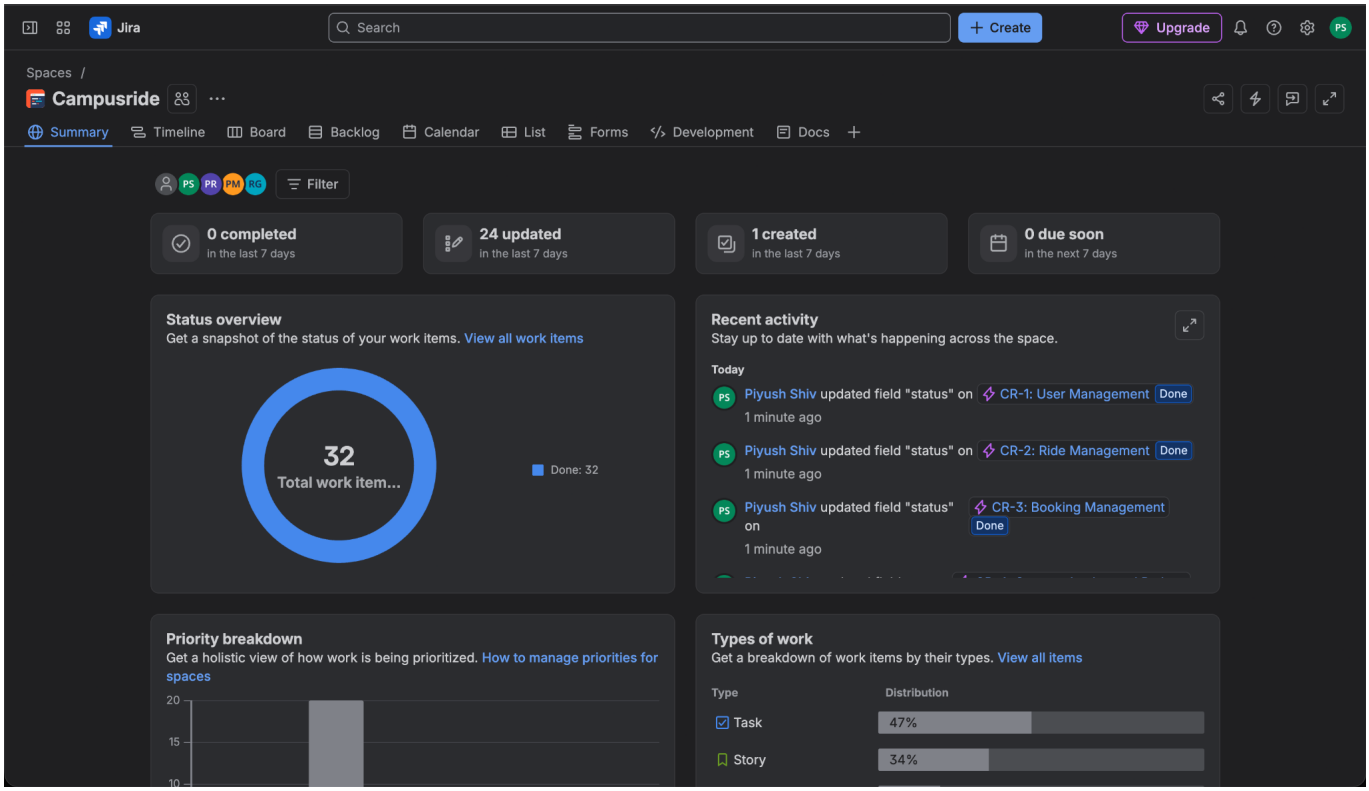

Additional Jira overview — epic statuses and work-item list

